WEEKLY PROJECT DASHBOARD

PRJ-DAI-03 / WEEK 18 / DATA DATE 22 SEP 2026

A3 EXECUTIVE SUMMARY

002 Overall Progress Position

19.12%
PLANNED

17.74%
ACTUAL

-1.38 pp

003 Executive Schedule Position

26 May 2027
Forecast completion

15 DAYS LATE
vs. baseline 11 May 2027

028 QA/QC Summary

5 DOCUMENTS
Open / closed status

008 Cumulative Planned vs Actual Progress

009 + 010 Weekly Progress & Week-on-Week Change



010 WEEK-ON-WEEK VARIANCE (percentage points)

W17	P: -0.042 pp	A: N/A
W18	P: -0.237 pp	A: +0.196 pp

013 Progress by Phase



014 Trades: Baseline Dates vs Actual Dates | Gantt

TRADE	BASELINE START - FINISH	ACTUAL START - LAST FINISH
Structural Works	01 Sep 26 - 26 Oct 26	06 Sep 26 - 28 Oct 26
Electrical	12 Sep 26 - 16 Nov 26	20 Sep 26 - 22 Nov 26
False Ceilings	23 Sep 26 - 07 Dec 26	04 Oct 26 - 17 Dec 26
Fire Protection	04 Oct 26 - 28 Nov 26	09 Oct 26 - 12 Dec 26
Glazing	15 Oct 26 - 19 Dec 26	23 Oct 26 - 21 Dec 26
Grouting	26 Oct 26 - 09 Jan 27	06 Nov 26 - 15 Jan 27
HVAC	06 Nov 26 - 31 Dec 26	11 Nov 26 - 10 Jan 27

SEVEN SELECTED TRADES | PROVISIONAL TRADE NAMES AND ILLUSTRATIVE GANTT DATES

033 Manpower by Resource

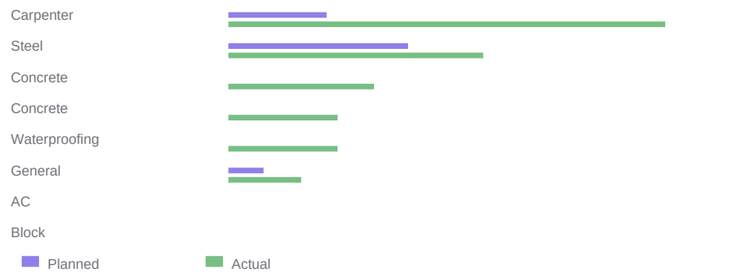

022 / 023 / 024 Engineering Status by Type

Original source counts by transmittal type

026 Engineering Submissions | 4-Week Trends

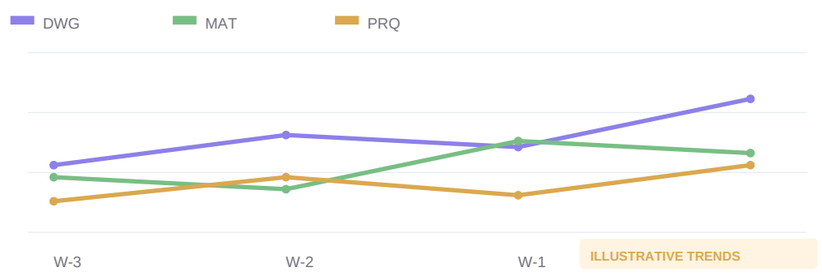

039 / 040 KPI Quantities

039 CUMULATIVE PLANNED vs ACTUAL



040 WEEKLY PLANNED vs ACTUAL

007 Major Construction, Engineering & Quality Exceptions

Project Completion Delayed
Forecast completion is 2027-05-26 against a pl
anned project completion of 2027-05-11, a cur

Engineering Submissions Overdue
78 of 438 engineering transmittals remain unsu
bmitted beyond their planned submission date,

Status C Transmittals Not Resubmitted
44 transmittals returned with Status C have no
t been resubmitted for more than 14 days.

Submittals Under Review Beyond 14 Days
25 engineering transmittals have remained unde
r review for more than 14 days, all of them S

DATA NOTE: Seven selected trades, provisional labels and illustrative dates; WGT-026 trends illustrative. Other values from stored Week 18 A
Weekly dashboard visual theme | Mockup, not a source-complete or CPM-verified report | A3 landscape
